


CMS Monthly Status Report -- Cal Poly Pomona

February-2003

Student Admin 8.0 Implementation Status Detail

Implementation:	Student Admin 8.0
Live Production:	
Go-Live # 1	1/12/04
Go-Live # 2	4/30/04
Go-Live # 3	6/30/04
Go-Live # 4	8/2/04
Project Status:	On Schedule
Impl'n Partner:	Cedar

Start Date	Milestone	Go-Live	End Date	Status
1/13/03	Academic Structure Defined	1	2/28/03	Complete
2/17/03	Course Catalog/Schedule Converted	1	7/11/03	In Progress
3/17/03	Applications Loaded	1	1/12/04	Not Started
3/17/03	New Student Admitted	1	1/12/04	Not Started
2/17/04	Transfer Credit Evaluated	4	8/2/04	In Progress
2/24/03	Financial Aid Awarded	2	4/16/04	In Progress
3/3/03	Student Bill Generated	4	8/2/04	Not Started
11/3/03	GL & A/P Interface Completed	2	4/30/04	Not Started
3/3/03	Payments Posted	4	8/2/04	Not Started
2/17/03	Student Registration	3	6/15/04	In Progress
2/24/03	Financial Aid Disbursed	3	6/11/04	In Progress
3/17/03	Student Degree Audited	3	6/4/04	Not Started
2/17/03	Grades Posted	4	8/2/04	In Progress
2/17/03	Student Academic Records Completed	4	8/2/04	In Progress
6/2/04	Implementation Phase Completed	4	8/2/04	Not Started

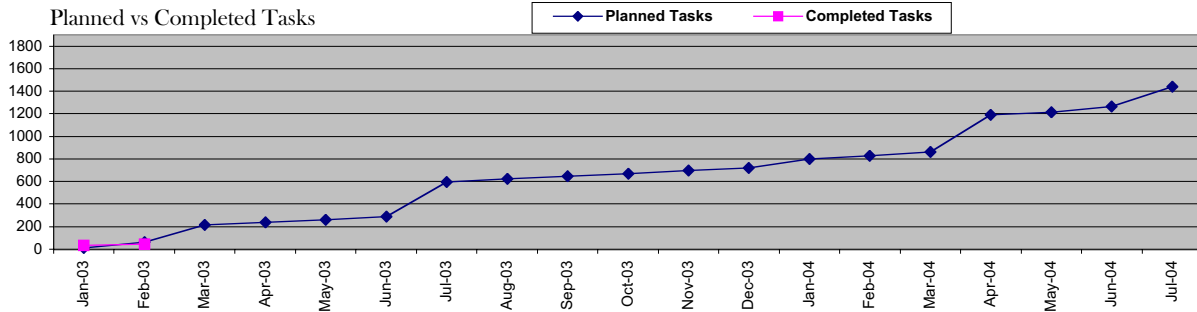

Recent Activity / Accomplishments (Last 30 Days):

- (1) Academic Structure IDP
- (2) Academic Structure Defined

Key Upcoming Activities (Next 30 Days):

- (1) Campus Community IDP
- (2) Student Records IDP

Current Issues / Concerns:

None to report
